

## Plastering Plus -Sample- Daily Report

Contractor: Plastering Plus      Manpower: 19      Weather: Rain 65 deg      6-17-14

<b>1. Contractor:</b> (Plastering Plus NW)	
<b>2. Description of work completed today:</b>	
<b>Stone:</b>	(2) Stone L2 West, scratch coat all East, flashing top of stone
<b>EIFS Foam:</b>	(0) Foam at screen wall L2 roof, v grooves, sand ready for mesh, patch L2 door roof w/ foam
<b>EIFS Mesh:</b>	(7) Mesh L6 phase 3, Skim L5 where dry (no scuppers)
<b>EIFS FINISH:</b>	(4) Too wet
<b>Foremen:</b>	(1) Weather protection, hardie details / backing
<b>MISC:</b>	(3) Sand, mix color, cleanup
<b>Scaffold:</b>	(0)
<b>Sealants</b>	(0)
<b>Hardie</b>	(2) L1 East complete
<b>3. Verbal Instructions or Comments:</b> (Input / conversations with other subs)	
Safety meeting, foremen's meeting. Cleanup. Keep roof clean, lots of rust, and sharp metal debris.	
Taked to A about roof tie off. Will meet him, Travis and Kyle tomorrow.	
Talked to Kyle about downspouts and scupper install off scaffold to keep flow going. He has materials and will follow us.	
<b>4. ACTION ITEMS: Schedule / Paperwork / Coordination Items:</b> (New, prior, resolutions, RFI's)	
OPEN: Monitor temp downspouts, Every Day – rain coming... Plastic on doors blew off over weekend, not effective. Recommend installing doors or plywood with hinges, esp on roof and exposed areas (electrical room) and areas under downspouts if downspouts aren't extended to ground. Roof membrane flapped over during weekend. Needs to be 100% corrected with Drywall and insulation installed!	
<b>5. Remarks: (Progress notes)</b>	
<b>Phase 1:</b> N/A.	
<b>Phase 2:</b> Skim coat complete to L4, Finish L5, Caulk scuppers	
<b>Phase 3:</b> Finish L6,5 and start 4. Caulking to start. Scuppers coordinated	
<b>6. Look Ahead:</b> (Next day): 6-18-14 Manpower = 19/20	
<b>*Stone:</b>	L1 West
<b>*Hardie:</b>	L5 West tower caulk and move to L5 East
<b>*EIFS:</b>	Skim coat complete at L3, finish complete to L4/5
<b>*Misc:</b>	Mix finish, shore scaffold at footings SE corner

Name: Brenan Filippini

Signature: \_\_\_\_\_

Date: 6-17-14




Skim coat L6, 5,4 North complete, 50% L3

Haride siding complete until windows are in L6 West



Color started at all elevations

Skim coat at L5 West where walls were wet from scupper. South L4/5 complete, West L5 and 50% L4 complete

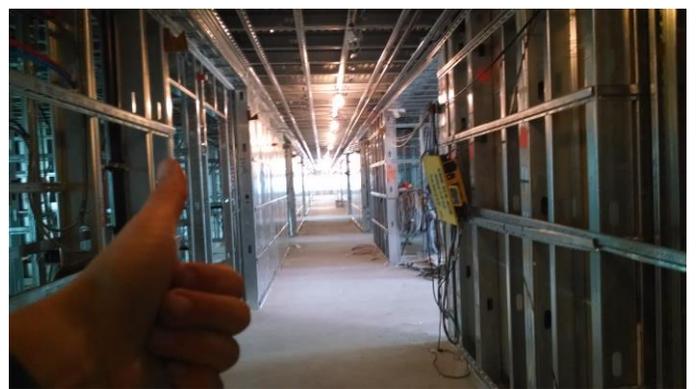

Trash inside at stairwell L5. I forgot to go back and get it....

L5 interior nice jobsite! I wished I was an inside worker this day (not really)
